



TRAM Governance Structures

Governance Structure

as agreed at Council 25 August 2011 and 2 September 2011

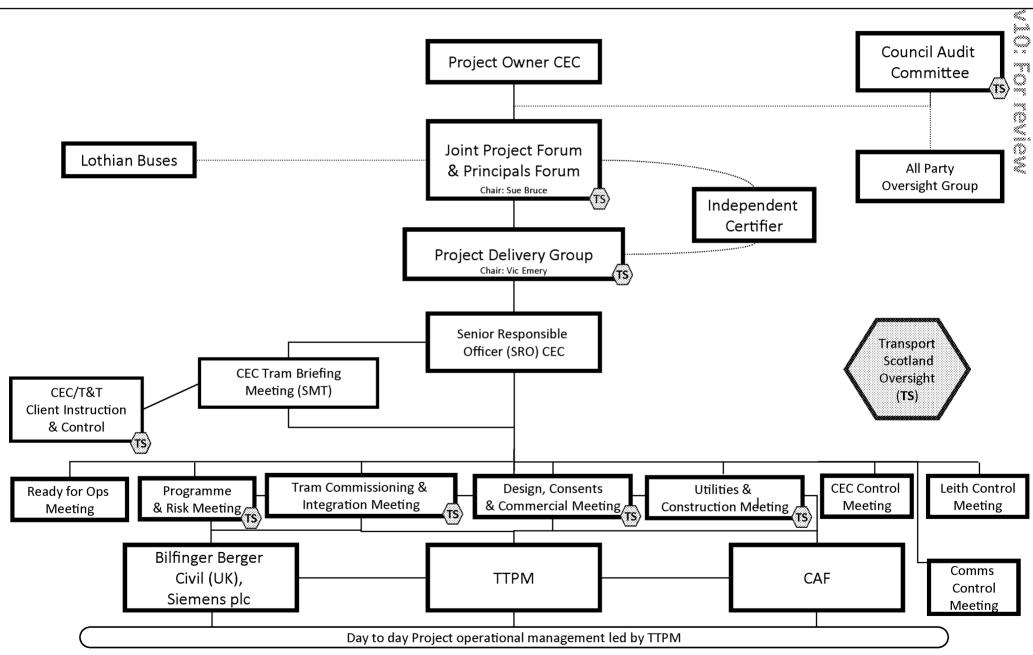

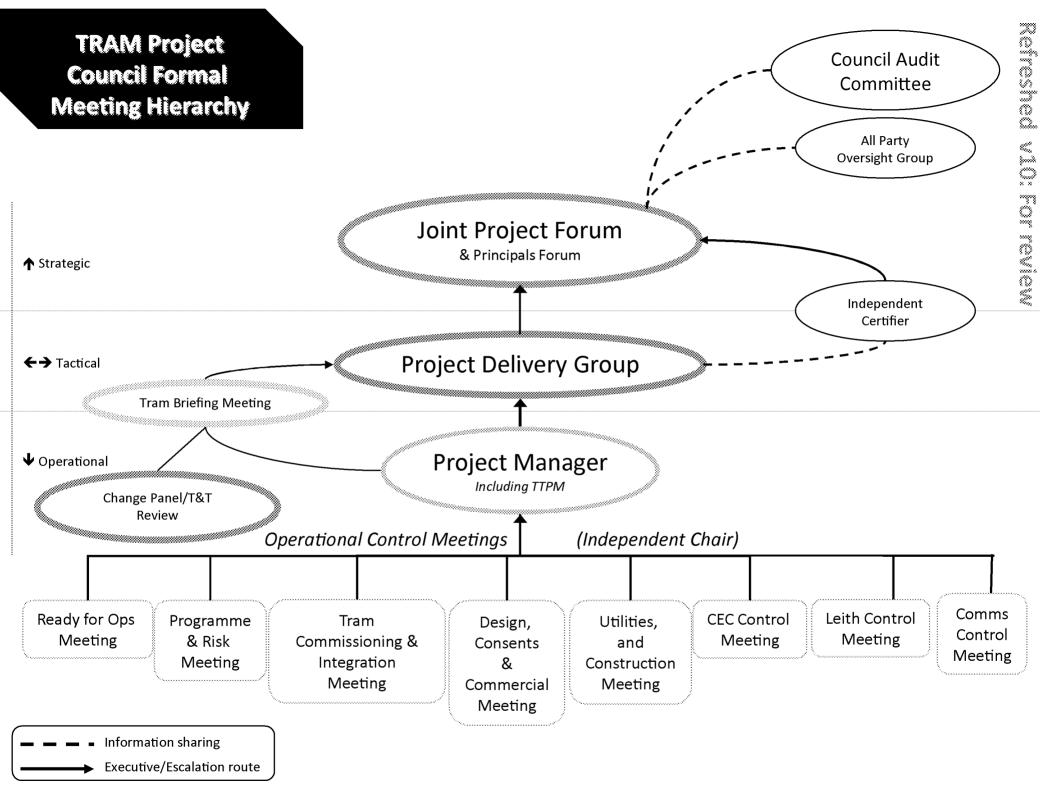

Governance Meeting Diary

Change Panel/

T&T Review

Tram Briefing

Meeting

Weekly

Governance Meeting Descriptors

TRAVIA ojeci Mestrij Destaljim

Agenda Issued

Meeting title: Joint Project Forum & *Principals Forum*

Chairmanship: Vice Chairmanship:	Council Chief Executive Vic Emery
Location for meeting:	Waverley Court
Day held	Wednesday
Frequency	Monthly/ Quarterly
Duration	1 hour 30 minutes
Meeting Purpose	To provide clear strategic leadership and direction to the project
Decisions expected	 Confirmation of project progress Resolution of escalated issues
Escalation	N/A
Reporting Route	1. Council Audit

2.

Committee

Three days in advance

Scottish Ministers

Standard Attendee List Principals Invited Quarterly Sue Bruce Dr Keysberg Vic Emery Dr Schneppendahl Alastair Maclean **Antonio Campos** Mark Turley **Dave Anderson** Colin Smith Martin Foerder Alfred Brandenburger Richard Garner Ainslie McLaughlin Chris Walton/Ian Craig Alan Coyle

Standard Agenda Items

Kelly Murphy/Lucy Adamson

- 1. Consolidated Project Update Highlight Report
- 2. Escalated Issues
- 3. Key Milestones due in next quarter
- 4. Communications

May Nacian Nacing Descriptor

Meeting title: Project Delivery Group

Chairmanship:

Vice Chair:

Location for meeting:

Day held

Frequency

Duration

Meeting Purpose

Decisions expected

Escalation

Reporting Route

Vice Chair Joint **Project** Forum Senior Responsible Officer

Waverley Court

Thursday

Monthly

2 hours

To manage the operational delivery of the project and report on progress against programme and budget.

- Confirmation of project programme progress
- Confirmation of project budget progress
- Identification of issues for Escalation.

Joint **Project** Forum

Joint Project Forum

Standard Attendee List

Vic Emery

Colin Smith

Bob McCafferty

Graham Porteous (TS)

Ian Craig

Julian Weatherley (T&T)

Gary Easton (T&T)

Rob Leech (T&T)

Alan Covle

Kelly Murphy

Lucy Adamson

- 1. Project Update Highlight Reports
 - a. Programme
 - b. Budget
- 2. Issues for Escalation
- 3. Communications

Titaly Project Media: Descriptor

Meeting title: Programme & Risk Meeting

Chairmanship:

Vice Chair:

Location for meeting:

Day held

Frequency

Duration

Meeting Purpose

Decisions expected

Escalation

Reporting Route

Independent Certifier

Alan Coyle

Lochside

Tuesdays

Programme Fortnightly/

Risk Monthly

1 hour

To ensure compliance with the contract programme and to mitigate and manage risk.

 Confirmation of compliance

• Escalation of non compliance

Management actions to control risk

• Escalation of risks that are manifesting themselves.

Project Delivery Group

1. CEC Internal Weekly Review Meeting

2. Project Delivery Group

Standard Attendee List and Distribution

Colin Smith Graham Robertson

Martin Foerder

Dominic Murphy

Kevin Russell

James Cowie

Steve Sharp

Alfred Brandenburger

Julian Weatherley

Gary Easton

Paul Robinson

Alan Coyle

Bob McCafferty

- 1. Items Programme Review
- 2. Risk Register Review
- 3. New Risks

TRAMProjec Massing Baresjorer

Meeting title: Tram Commissioning & Integration Meeting

Chairmanship: Independent Certifier Vice Chair: Alan Coyle **Location for meeting:** Lochside Day held Wednesday / Thursday **Frequency** Monthly **Duration** 1 hour **Meeting Purpose** To ensure efficient delivery, commissioning and integration of the total tram system to an operational state. **Decisions** expected · Acceptance of handover criteria. • Compliance with ROGs Compliance with commissioning Programme Health and Safety compliance of system **Escalation** Project Delivery Group **Reporting Route CEC Internal Weekly Review Meeting** 2. Project Delivery Group

Standard Attendee List and Distribution Colin Smith Steve Westwood	
Martin Foerder	Michael Wilken
Stefan Rotthaus	Patrick Scully
Jim Donaldson	Martyn Ayres
David Steele	William Delaney
Alfred Brandenburger	Eddie Inglis
Kevin Russell	John White
Julian Weatherley	Dominic Murphy
Pall Palsson	

- 1. Acceptance Criteria
- 2. Commission Progress
- 3. System Testing
- 4. Programme
- 5. Health and Safety

Tiray/Projes Masang Dersijos

Meeting title: Design, Consents & Commercial Meeting

Chairmanship: Independent Certifier

Vice Chair: Alan Coyle

Location for Lochside meeting:

Day held Tuesday/Wednesday/Thursday

Frequency Fortnightly

Duration 1 hour

Meeting Purpose To ensure capture any potential

requirement for design change; To develop the scope of any change orders that arise; To monitor the progress of any change orders issued; To agree the originator of the change and the value/cost of the change; To review resource allocation and records reconciliation; To confirm Valuation and Certifiers Review (Every other Meeting)

Decisions expected

All draft and agreed change orders and their cost consequences are recorded and reported to the client and the contractor.

Escalation

Project Delivery Group

Reporting Route

1. CEC Internal Weekly Review Meeting

2. Project Delivery Group

Standard Attendee List and Distribution

Colin Smith Alan Coyle

Simon Nesbitt Julian Weatherley

Martin Foerder Martyn Ayres

David Gough Gary Easton

David Steele Rob Leech

Kevin Russell Shirley Mushet

Alfred Brandenburger Dominic Murphy

Axel Eickhorn Scottish Water (part)

Bob McCafferty

Andy Conway

Michael Wilken

Shabu Dedhar

- 1. Review of design consents Report
- 2. Commercial Consequences of Change and liability identification
- 3. Monthly Valuation and Certifiers Review

Magnin: Darengton

Meeting title: Utilities, Princes Street and Construction Meeting

Chairmanship: Independent Certifier

Vice Chair: Alan Coyle

Lochside Location:

Day held Tuesday

Monthly **Frequency**

Duration 1 hour

To ensure coordination of approach between **Meeting Purpose**

the contractor, utilities contractors and design solutions; To ensure that there is efficient working on Princes Street while interfacing with

city requirements; To ensure that

communication with stakeholders is maintained: To clear construction blockers and to ensure the

quality systems, health and safety and NCR reporting is compliant with employer's

requirements.

Decisions

Confirmation of coordination of utilities works: Escalation of non-conformity of utilities works; expected Confirmation of efficient management of

> construction work; Confirmation of any specific communication issues for stakeholders.; Confirmation that construction activity is

meeting employer's requirements.

Escalation Project Delivery Group

Reporting Route CEC Internal Weekly Review Meeting

> 2. Project Delivery Group

Standard Attendee List and Distribution

Colin Smith Graham Robertson

Jim Donaldson Julian Weatherley

Martin Foerder **Gary Easton**

Kevin Russell Rob Leech

David Steele Stephen Lewcock

Alfred Brandenburger **Shirley Mushet**

Klaus Dieker Network Rail (part)

Clive Arbuckle

Andy Conway

Alan Coyle

Dominic Murphy

- 1. Identification of utilities clashes
- 2. Solution coordination
- 3. Traffic management
- 4. Stakeholder requirements
- 5. **Resolution of Construction Blockers**
- 6. Review of NCR Register

Refreshed VID: For review

TRAM Project Maanny Baserjois

Meeting title: CEC Control Meeting

Chairmanship:Bob McCaffertyVice Chair:Colin SmithLocation for meeting:LochsideDay heldThursdayFrequencyMonthlyDuration1 hour

Meeting Purpose

To ensure all consents,
approvals and tram ancillary
issues are actioned
timeously.

Decisions expected

• Identification of issues for escalation.

• Internal approval from within CFC.

Escalation

Reporting Route

Tram Briefing

1. CEC Internal Weekly Review Meeting

Standard Attendee List and Alternate Meeting Attendee List

Colin Smith

Alan Coyle

Bob McCafferty

Michelle Coyle

Andrew Renwick

Francis Newton

Secretarial support

- 1. TROs
- 2. Planning Approvals
- 3. Technical Approvals
- 4. Air Quality
- 5. Asset Demarcation and Hand back

TitalVIProjed Mesang Desagoror

Meeting title: Communications Control Meeting

Chairmanship: Vice Chair:

Lochside

Colin Smith

Alan Covle

Location for meeting:

Thursday

Frequency

Day held

Monthly

Duration

1 hour

Meeting Purpose

To examine and control the three month comms

lookahead.

Decisions expected

 Project support and approval of the three month comms lookahead.

Escalation

Tram Briefing

Reporting Route

1. CEC Internal Weekly Review Meeting

Standard Attendee List and Alternate Meeting Attendee List

Colin Smith

Jim Donaldson

Kevin Russell

David Steele (DS)

Alan Coyle

Kelly Murphy

Caroline Trainer

Julie Smith

Lucy Adamson

Secretarial Support

- 1. Comms 3 month look ahead plan
- 2. Press enquires
- 3. Incident forum reports

TRAM Project Meeting Descriptor

Meeting title: LB Control Meeting

- (Ready for Operations)

Chairmanship:

Vice Chair:

Location for meeting:

Day held

Frequency

Duration

Meeting Purpose

Decisions expected

Escalation

Reporting Route

Alan Coyle Colin Smith

Gogar Depot

Thursday

Monthly

1 hour

To ensure smooth transition

from construction to

operations.

• Identification of issues for

escalation.

 Issues requiring liaison and instruction to

contractors .

• Interface with Tram and

CEC control meetings

Tram Briefing

Joint Project Delivery

Group/Joint Project Forum

1. CEC Internal Weekly Review Meeting

Standard Attendee List and Alternate Meeting Attendee List

Colin Smith

Alan Coyle

Ian Craig

Bill Campbell

Kelly Murphy

Bill Devlin

Julie Smith

Eddie Inglis

Norman Strachan

Liz Parkes

John White

Secretarial support

- 1. H&S
- 2. Snagging and Defects
- 3. Demarcation of site
- 4. Testing and commissioning
- 5. Security
- 6. Finance and Procurement
- 7. Visitor protocol and comms

Titaly kojed Masing Descriptor

Meeting title: Tram Briefing Meeting

Chairmanship: Vice Chair:	Council Chief Executive Vic Emery
Location for meeting:	Waverley Court
Days held	Tuesday and Thursday
Frequency	Weekly
Duration	1 hour
Meeting Purpose	To provide clear operational oversight as client, to provide challenge to issues and change requests and to be the client sign off point for change requests.
Decisions expected	 Identification of issues for escalation. Confirmation of potential changes to be actioned through formal change process Client agreement of Change request applications
Escalation	N/A
Reporting Route	1. Project Delivery Group

Standard Attendee List and Alternate Meeting Attendee List	
Tuesdays and Thursdays:	Alternate Thursdays only:
Sue Bruce	Graham Porteous
Vic Emery	Julian Weatherley
Ainslie McLaughlin	Gary Easton
Alastair Maclean	Rob Leech
Mark Turley	
Dave Anderson	
Colin Smith	
Alan Coyle	
Bob McCafferty	
Lucy Adamson	

Standard Agenda Items

1. Governance

Kelly Murphy

- 2. Project Management
- 3. Operational Issues
- 4. Communications
- 5. Change & Finance Report

Alternate Week Agenda Items

- 1. Turner & Townsend Report *Client only*
- 1. Client Instructions
- 2. Finance
- 3. Consents and Approvals
- 4. Communications
- 5. Political Feedback & Updates

TRAW Project Weeting Descriptor

Meeting title: Leith Control Meeting

Chairmanship:

Vice Chair:

Location for meeting:

Day held

Frequency

Duration

Meeting Purpose

Decisions expected

Escalation

Reporting Route

Alan Coyle Colin Smith

Lochside

Thursday

Monthly

1 hour

To ensure all work packages are co-ordinated from a technical and comms perspective.

Identification of issues for escalation.

Tram Briefing

1. CEC Internal Weekly Review Meeting

Standard Attendee List and Alternate Meeting Attendee List

Colin Smith

Alan Coyle

Bob McCafferty

Rob Leech

Richie Hailes/Steve Jackson

Shane MacKenzie

Andy Conway

Andrew Easson

Andy Scott

Chris Wilson

Kelly Murphy

Secretarial support

- 1. Scope
- 2. Programme
- 3. Lindsay Road
- 4. Comms

TRANSPORT

Meeting title: CEC/T&T Client Instruction & Control

Chairmanship:	Colin Smith (Control/Instruction) Alan Coyle (Change) Bob McCafferty (TT Report)
Location for meeting:	Lochside
Day held	Monday
Frequency	Weekly
Duration	1 hour
Meeting Purpose	To challenge and administer
meeting i dipose	change. To ensure the client is aware of all relevant project matters. To issue client instruction to TTPM.

• Change Approval

• Client Instruction

Escalation Tram Briefing

Decisions expected

Reporting Route 1. CEC Internal Weekly **Review Meeting**

Standard Attendee List and Alternate Meeting Attendee List

Colin Smith

Alan Coyle

Bob McCafferty

Julian Weatherley

Gary Easton

Rob Leech

Ed Foster

Dominic Murphy

Clive Arbuckle

Secretarial support

- Approval of previous minutes 1.
- 2. H&S
- 3. Change
- 4. Review of TT sub meetings
- 5. CEC Control Review/Client Instruction
- 6. Utilties
- 7. York Place

Other Meeting Descriptors

o ditamberojse o Messing Desembro

Meeting title: All Party Oversight Group

Chairmanship: Vice Chair:	Council Leader Senior Responsible Officer
Location for meeting:	City Chambers (room TBC)
Day held	Monday
Frequency	Monthly
Duration	1 hour
Meeting Purpose	To provide updates on Tram project progress, current issues and the Open for Business activities
Decisions expected	 Confirmation of project progress Identification of additional information required Confirmation of Open for Business activities
Escalation	N/A
Additional Briefings	Regular electronic briefing to be issued to elected members between meetings
	•

Standard Attendee List	
Councillor Dawe (LD)	Sue Bruce
Councillor Cardownie (SNP)	Dave Anderson
Councillor Burns (LAB)	Alastair Maclean
Councillor Balfour (CON)	Alan Coyle
Councillor Burgess (GR)	Kelly Murphy
Councillor Mackenzie (LD)	Bob McCafferty
Councillor Hinds (LAB)	Colin Smith
Councillor Jackson (CON)	
Councillor Johnstone (GR)	

- 1. Project Update Highlight Report
- 2. Current Issues
- 3. Open for Business Update

Titaly Project Vicesing Desemble

Meeting title: City Centre Elected Members Briefing

Chairmanship:	Director of City Development
Location for meeting:	Tbc
Day held	Tbc
Frequency	Monthly
Duration	30 minutes
Meeting Purpose	To ensure city centre elected Members remain informed of progress on the Tram Project and to allow a formal channel through which key issues can be raised.
Decisions expected	None
Escalation	Tram Briefing Meeting
Reporting Route	 Project Delivery Group Tram Briefing Meeting

Standard Attendee List

Joanna Mowat

Charles Dundas

Alastair Rankin

Kelly Murphy

Dave Anderson

- 1. Programme Update
- 2. Key Milestones due in next month
- 3. Open for Business Programme
- 4. Issues arising
